

Work Order ID 158292***158292***

Page 1

Friday, March 17, 2017 1:07:47 PM

Item ID: D4634-145

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Aft, Center Ceiling Replacement Panel Assembly

Start Date: 3/20/2017 Start Qty: 1.00 ***1***

Cust Item ID:

Required Date: 3/28/2017 Req'd Qty: 1.00 ***1***

Customer:

Reference: SCHEDULED

Approvals: Process Plan:

DAS
21
9-89

Date: MAR 17 2017

Tooling:

Date:

Run Start ***NR1***

QC:

Date:

SPC (Y/N):

Date:

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr

Revision Nbr

D4634

G

100

0.00

100

HandThermo

Memo

0.83

Hand Finishing Thermoforming

Pick Kit

DAS
07
9-89

17/03/22

110

0.00

110

Small Fab

Memo

1.31

Small Fab

Assemble as per Dwg D4634-145

DAS
07
9-89

17/03/23

1- Scuff bonding surface to eliminate in-perfections and increase bonding and clean with wash& wipe

2- Locate and glue down Channel Assy, angles, brackets, and mounting pads using 3M Plastic welder II.

Batch # M132023Expiry Date 12/05/24

3- Apply labels as per Dwg. and seal with 3M 3950 edge sealer

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐						OTHER : ☐	

158292

Friday, March 17, 2017 1:07:47 PM

Accept

N900040100

Setup Start *NS1*

Stop *NS2*

Item Name: Aft, Center Ceiling Replacement Panel Assembly

Start Date: 3/20/2017 **Start Qty:** 1.00 ***1***

Cust Item ID:

Required Date: 3/28/2017 **Req'd Qty:** 1.00 *** 1 ***

Customer:

Reference: SCHEDULED

Run Start *NR1*

Approvals: _____ **Process Plan:** _____ **Date:** _____ **Tooling:** _____ **Date:** _____

Stop *NR2*

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

[illegible]

mc
17-3-24

DQA: _____ Date: _____

**WORK ORDER NON-CONFORMANCE / UPDATE**

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER : _____							
Misidentified ☐	Past Due ☐								

Picklist Print

Friday, March 17, 2017 1:07:56 PM

Page 1

4

Work Order ID: 158292

158292

Parent Item: D4634-145

D4634-145

Parent Item Name: Aft, Center Ceiling Replacement Panel Assembly

Start Date: 3/20/2017

Required Date: 3/28/2017

Start Qty: 1.00

Required Qty: 1.00

Comments: IPP Rev. A 12/08/09 New Issue DL
 12/11/08 Document release DL VERIFIED BY:JLM
 Dwg Update DL verf: DD
 DL
 DL
 DL
 IPP Rev B
 IPP Rev C 13/07/09
 IPP Rev D Dwg Update 13/12/23
 IPP REV E Dwg update 14/01/09
 IPP Rev F Dwg. update 14/02/03
 IPP Rev G Dwg. Update 15/01/27 DL

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
D4636-5 *D4636-5* Bracket		Manufactured	No			100	Each	40.0000	1	1			DAS 07 9-89 17/03/23
				<u>Location</u>				<u>Loc Qty</u>					
				ST115				40					
				154779				16					
				154916				24					
D4712-1 *D4712-1* Bracket		Manufactured	No			100	Each	5.0000	1	1			DAS 07 9-89 17/03/23
				<u>Location</u>				<u>Loc Qty</u>					
				MF004				5					
				149103				5					
D5021-5 *D5021-5* Foam, Center Panel, Aft		Manufactured	No			100	Each	0.0000	1	1			DAS 07 9-89 17/03/23
				<u>Location</u>				<u>Loc Qty</u>					

~~158292~~ 158412

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
								Completed By 	
								Lead hand / Supervisor Approval Verification 	
QC / QA Coordinator Approval 									

Root Cause				FAULT CATEGORY							
Environment ☐		No Re-verification ☐		Pressure/Forced ☐		Temperature/Cure ☐		Power Loss/Surge ☐		Positioned Wrong ☐	
Design ☐		Operator ☐		Bending ☐		Set-up ☐		Folio/Program ☐		Outside Dimensions ☐	
Doc/Data ☐		Offset/Setup ☐		Centre Not Concentric ☐		BOM/Route ☐		Grain ☐		Over/Under tolerance ☐	
Equip/Tooling ☐		Supplier ☐		Cracks ☐		Broken/Damage/Defect ☐		Weld ☐		Part Incorrect ☐	
Handling/Pre ☐		Training ☐		Crimp/Kink/Ripple/Wave ☐		Inspection Incomplete/Unqualified ☐		Wrong Stock Pulled ☐		Part Lost/Missing ☐	
Material ☐		Use for Testing ☐		Cuffs ☐		Contamination ☐		Out of Sequence ☐		Part Moved ☐	
Internal Transport ☐		Poor Information ☐		Crushing ☐		Countersink ☐		Off-set ☐		Drawing ☐	
Tribal Knowledge ☐		Rushing ☐		Heat Treat ☐		Cut Too Short ☐		Mislabeled ☐		Finish ☐	
LOA ☐		Product Improvement ☐		Wave/Twist in Tube ☐		Instructions Incomplete/Unclear ☐		Fit/Function ☐		Misread ☐	
Substation ☐		Process Improvement ☐		Marks/Chatter ☐		Drill Holes ☐		Misaligned/off center ☐		Turning Sequence ☐	
Past Expiry Date ☐		Manufacturing Process ☐		OTHER :							
Misidentified ☐		Past Due ☐									

Picklist Print

Friday, March 17, 2017 1:07:56 PM

Work Order ID: 158292

158292

Parent Item: D4634-145

D4634-145

Parent Item Name: Aft, Center Ceiling Replacement Panel Assembly

Start Date: 3/20/2017

Required Date: 3/28/2017

Start Qty: 1.00

Required Qty: 1.00

MS20426AD3-4

Purchased

No

100

Each

8,464.000

4

4

**

MS20426AD3-4

RIVET

DAS
07
9-89

17/03/23

Location

Loc Qty

Loc Code

GA

6558

m134294

1933

m136444

4625

ST312

1906

m134294

1906

MS20426AD4-6

Purchased

No

100

Each

1,507.000

2

2

**

MS20426AD4-6

Rivet

DAS
07
9-89

17/03/23

Location

Loc Qty

Loc Code

GA

715

M134502

25

M136537

690

ST311

792

M136537

792

MS21059L08

Purchased

No

100

Each

172.0000

2

2

**

MS21059L 08

Nut

DAS
07
9-89

17/03/23

Location

Loc Qty

Loc Code

ST300

172

m134943

72

m136554

100

D4634-5

Manufactured

No

100

Each

0.0000

1

1

**

D4634-5

Aft, Center Ceiling Panel

DAS
07
9-89

17/03/23

158293.

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
Root Cause		FAULT CATEGORY							
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐	OTHER : ☐			

Picklist Print

Friday, March 17, 2017 1:07:56 PM

Work Order ID: 158292

158292

Parent Item: D4634-145

D4634-145

Parent Item Name: Aft, Center Ceiling Replacement Panel Assembly

Start Date: 3/20/2017

Required Date: 3/28/2017

Start Qty: 1.00

Required Qty: 1.00

DAS
07
9-89

D4647-1

Manufactured No

100

Each

9.0000

1

1

**

D4647-1

Doubler

17/03/23

Location

Loc Qty

Loc Code

MF004

7

155284

7

ST116

2

154781

2

D4664-5

Manufactured No

100

Each

51.0000

6

6

**

D4664-5

Spacer

DAS
07
9-89
17/03/23

Location

Loc Qty

Loc Code

MF004

51

154825

21

155824

30

D4732-17

Manufactured No

100

Each

1.0000

1

1

**

D4732-17

Label

DAS
07
9-89
17/03/23

Location

Loc Qty

Loc Code

MF005

1

149138

1

8/2/2017

D4732-23

Manufactured No

100

Each

7.0000

1

1

**

D4732-23

Label

DAS
07
9-89
17/03/23

Location

Loc Qty

Loc Code

MF005

7

123211

7

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval 	
Description Work Order Deviation				Disposition					
								Completed By 	
								Lead hand / Supervisor Approval Verification 	
QC / QA Coordinator Approval 									

Root Cause				FAULT CATEGORY																																																											
Environment ☐	Design ☐	Doc/Data ☐	Equip/Tooling ☐	Handling/Pre ☐	Material ☐	Internal Transport ☐	Tribal Knowledge ☐	LOA ☐	Substation ☐	Past Expiry Date ☐	Misidentified ☐	No Re-verification ☐	Operator ☐	Offset/Setup ☐	Supplier ☐	Training ☐	Use for Testing ☐	Poor Information ☐	Rushing ☐	Product Improvement ☐	Process Improvement ☐	Manufacturing Process ☐	Past Due ☐	Pressure/Forced ☐	Bending ☐	Centre Not Concentric ☐	Cracks ☐	Crimp/Kink/Ripple/Wave ☐	Cuffs ☐	Crushing ☐	Heat Treat ☐	Wave/Twist in Tube ☐	Marks/Chatter ☐	Temperature/Cure ☐	Set-up ☐	BOM/Route ☐	Broken/Damage/Defect ☐	Inspection Incomplete/Unqualified ☐	Contamination ☐	Countersink ☐	Cut Too Short ☐	Instructions Incomplete/Unclear ☐	Drill Holes ☐	Power Loss/Surge ☐	Folio/Program ☐	Grain ☐	Weld ☐	Wrong Stock Pulled ☐	Out of Sequence ☐	Off-set ☐	Mislabeled ☐	Fit/Function ☐	Misaligned/off center ☐	Positioned Wrong ☐	Outside Dimensions ☐	Over/Under tolerance ☐	Part Incorrect ☐	Part Lost/Missing ☐	Part Moved ☐	Drawing ☐	Finish ☐	Misread ☐	Turning Sequence ☐
																								OTHER : ☐																																							

Picklist Print

Page 4

Friday, March 17, 2017 1:07:56 PM

Work Order ID: 158292

158292

Parent Item: D4634-145

D4634-145

Parent Item Name: Aft, Center Ceiling Replacement Panel Assembly

Start Date: 3/20/2017

Required Date: 3/28/2017

Start Qty: 1.00

Required Qty: 1.00

D4732-27

Manufactured No

100

Each

7.0000

1

1

**

D4732-27

Label

DAS
07
9-89

17/03/23

Location

Loc Qty

Loc Code

MF005

7

123213

7

100

Each

662.0000

9

9

**

MPNY-750S-9-C

Purchased

No

MPNY-750S-9-C

Mounting Pad

DAS
07
9-89

17/03/23

Location

Loc Qty

Loc Code

ST569

662

M130423

662

9

DQA: _____ Date: _____




WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐


Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval 	
Description Work Order Deviation				Disposition					
								Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	

Root Cause			FAULT CATEGORY							
Environment	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐	Power Loss/Surge	☐	Positioned Wrong
Design	☐	Operator	☐	Bending	☐	Set-up	☐	Folio/Program	☐	Outside Dimensions
Doc/Data	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐	Grain	☐	Over/Under tolerance
Equip/Tooling	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐	Weld	☐	Part Incorrect
Handling/Pre	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐	Wrong Stock Pulled	☐	Part Lost/Missing
Material	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐	Out of Sequence	☐	Part Moved
Internal Transport	☐	Poor Information	☐	Crushing	☐	Countersink	☐	Off-set	☐	Drawing
Tribal Knowledge	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐	Mislabeled	☐	Finish
LOA	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐	Fit/Function	☐	Misread
Substation	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐	Misaligned/off center	☐	Turning Sequence
Past Expiry Date	☐	Manufacturing Process	☐	OTHER :						
Misidentified	☐	Past Due	☐							

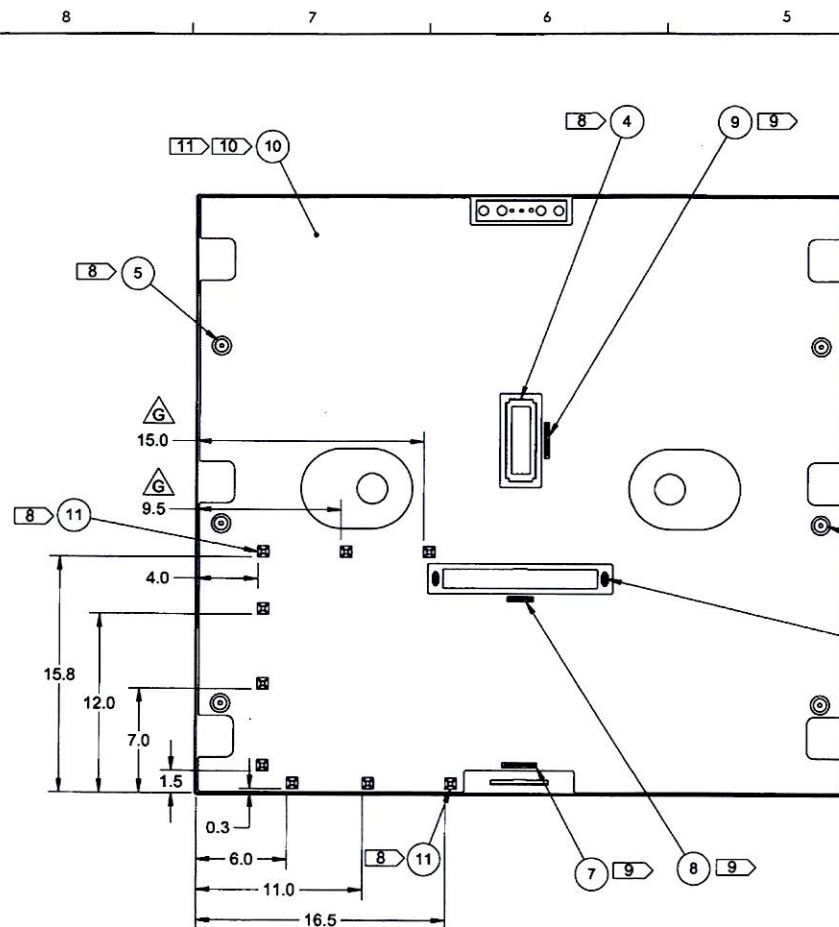

ITEM	QTY	P/N	DESCRIPTION
1	X	D4634-145	AFT, CENTER CEILING REPLACEMENT PANEL ASSY
2	1	D4634-5	AFT, CENTER CEILING PANEL
3	1	D4636-5	BRACKET
4	1	D4647-1	DOUBLER
5	6	D4664-5	SPACER
6	1	D4712-1	BRACKET
7	1	D4732-17	LABEL
8	1	D4732-23	LABEL
9	1	D4732-27	LABEL
10	1	D5021-5	FOAM, CENTER PANEL, AFT
11	9	MPNY-750S-9-C	MOUNTING PAD
12	4	MS20426AD3-(4)	RIVET, SOLID, CSK
13	2	MS20426AD4-(6)	RIVET, SOLID, CSK
14	2	MS21059L08	NUT PLATE

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 158292
MS
1703-17

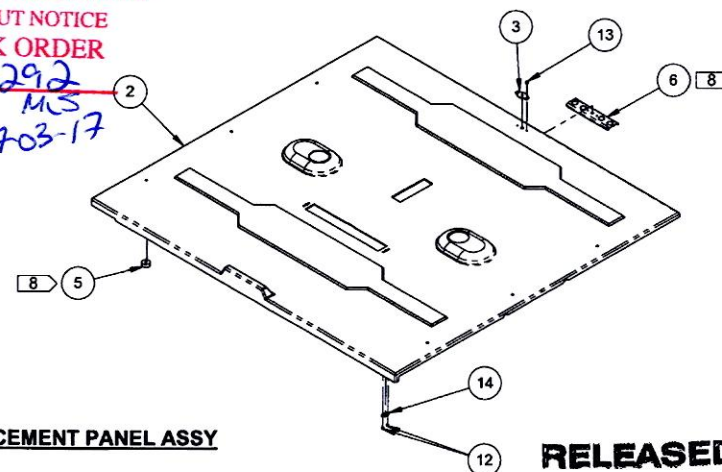

D4634-145 AFT, CENTER CEILING REPLACEMENT PANEL ASSY

NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: N/A
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: N/A
- 7) WEIGHT: N/A
- 8) APPLY A BEAD (0.20 TO 0.30 WIDE) OF DEVCON PLASTIC WELDER II (0.25 INSIDE OF BOTH EDGES OF PART) TO BOND D4647-1 & MPNY-750S-9C. WAIT FOR 2 TO 4 HOURS FOR FUNCTIONAL CURE.
- 9) LOCATE D4647-1 IN LINE WITH RECTANGULAR OPENING
- 10) LOCATE LABELS AS SHOWN, SEAL LABELS USING 3950 EDGE SEALER OVER LABEL TOP SURFACE
- 11) APPLY AN EVEN COAT OF 3M SCOTCH WELD 1300L CONTACT ADHESIVE TO BOND D5021-5 FOAM CORE TO INSIDE OF PANEL
- 12) CENTER D5021-5 FOAM ON D4634-5

RELEASED
2015 JAN 26

APPROVED	DESIGN	RF	DART AEROSPACE LTD	
	DRAWN	RF	HAWKESBURY, ONTARIO, CANADA	
	CHECKED	AK	DRAWING NO.	REV. G
	MFG. APPR.	DL	D4634	SHEET 9 OF 17
	APPROVED	HS	TITLE	SCALE
	DE APPR.	DS	CENTER CEILING PANELS	NTS
	DATE	14.11.28	COPYRIGHT © 2012 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL, AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMING OR COMMUNICATED TO ANY OTHER PERSON WITHOUT IT WRITTEN PERMISSION FROM DART AEROSPACE LTD.				
